

San Mauricio Mining Company

H. L. BARR

General Superintendent

The gross production at San Mauricio during February was ₱173,491.06, a total of 4,265 tons of ore having been milled. The recovered value was ₱40.68 per ton and the percentage of extraction was 91.8%.

Development

A total of 454 feet was advanced in operating development and 675 feet in capital development, a grand total of 1,129 feet for the month.

At the San Mauricio mine, the new Main Shaft was sunk 45 feet in hard granite gneiss and was 251 feet deep February 28. The old shaft was sunk 35 feet in hard granite gneiss and was

477 feet deep by the end of the month.

The Santa Monica Shaft was sunk 43 feet in hard granite gneiss and was 143 feet deep at the end of the month.

General

The mill operated satisfactorily throughout the month.

The results of the diamond drilling on the Santa Ana Vein have been very satisfactory to date.


The 150-ton fuel oil tank for the power plant was completed during the month, as was Staff House B of the native staff camp.

Work has been started on the erection of the No. 3 Allen Engine.

HENDY

Always Dependable

All Ways The Best

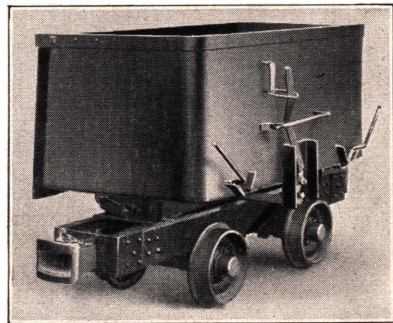

NEW HENDY MINE CAR

Think of mine cars and you think of HENDY—builders of durable Mätteson type cars for years. Look at HENDY'S New Mine Car and note these improvements:—Levers point upward, away from trackside interference, with stops for holding doors open or latched. Welded body construction increases strength. "Metal Lead" non-scalling paint prolongs wear.

The NEW HENDY CARS, designed for all ore, rock, or dirt moving, are suited to hand tramping, or hauling by mule or locomotive. Low-mounted for easy hand-loading. Available in many sizes. Rectangular, U-shape, V-shape, or Gable-bottomed bodies. "Dustproof", full floating axles, regularly fitted with roller bearings. HENDY special chilled long wearing wheels.

Write for detailed information

JOSHUA HENDY IRON WORKS

California

206 Sansome Street

San Francisco
